

FY27 CAO Priority

France Entity Migration to Oracle

Project Kickoff


21st May 2026

Agenda

Discussion Topic
Leadership Remarks
Project Overview
Project Scope
Timeline & Workshop Overview
Team & Governance
Next Steps & QA

Leadership Remarks

Mícheál Kelliher - International Controller

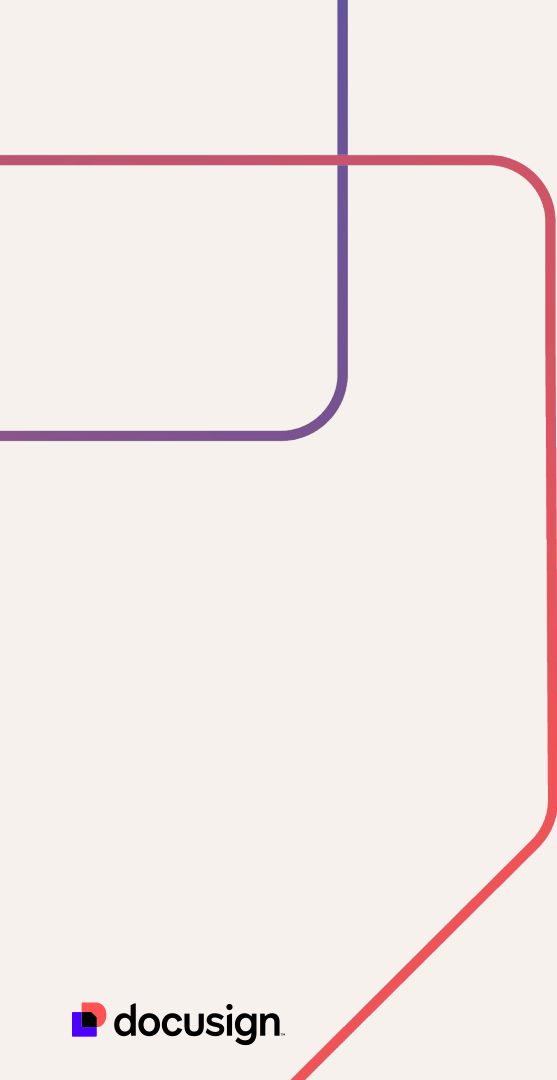

Project Overview

France Entity Migration Project Overview



Objectives

Migrate France legal entity accounting processes and data from Sage to Global Oracle Fusion Platform

AND

Migrate remaining France active customer contracts to DocuSign EMEA (Global Oracle Fusion Platform)



Opportunity

By migrating the France legal entity and customer contracts to Global Oracle Fusion Platform, we will:

- **Decommission legacy systems** by retiring the local sage ERP
- **Mitigate compliance risks** through globalized AP workflows, improved SODs, and standardized global SOX controls
- **Standardize financial reporting** by aligning R2R process under a unified global chart of accounts
- **Enable data transparency** with real-time access to DS France accounts for the corporate and FP&A teams
- **Drive operational efficiency** by automating accounting workflows and eliminating manual reporting

Project Scope

High Level Project Scope

French Legal Entity Migration

Sage to Oracle

- Enterprise Structure
- Record to Report (R2R)
- Procure to Pay (P2P)
- French Supplier Onboarding

Both Grant Thornton and Docusign will lead this workflow

E-Invoicing (France Only)

Localized Compliance

Deployment of mandatory e-invoicing solutions specifically for French statutory requirements.

Grant Thornton will lead this workflow

Contract Migration

DS France to DS EMEA

Active contract migration from DS France to DS EMEA legal entity

Docusign will lead this workflow

More insights to be provided in the upcoming scope commit.

French Localization Review

Grant Thornton will drive the discovery for the French localization assessment to ensure both US GAAP and French GAAP requirements are supported within one single, compliant, and efficient Oracle solution.

Key Objectives

br
us
h

Solution Design

Establish a clear solution design to support French GAAP and statutory requirements within Oracle.

sy
nc

Global Alignment

Ensure alignment with Docusign's global Oracle architecture and US GAAP priorities.

rul
e

Gap Analysis

Define key decisions, gaps, localization needs, and integration impacts before implementation.

m
ap

Future Roadmap

Create a high-level roadmap, resource plan, and future-state architecture for the France rollout.

Grant Thornton: Scope & Key Activities

Scope

Enterprise Structure

- Enterprise
- Legal entity
- Business Unit
- Accounting key
- Accounting calendar
- Currency
- Subledger Accounting Rules (SLA)
- Primary & Secondary Ledgers
- Chart of Accounts

Report To Record (R2R)

- General Accounting
- Fixed Assets & depreciation
- Intercompany Management
- VAT
- Closing
- Tax & Reporting

Procure To Pay (P2P)

- Procurement
- Accounts payables (AP)
- Reporting

Cash Management

- Payments
- Bank reconciliation

Project management

- Capital Projects

Focus on e-invoicing (dedicated workshops)

- Invoicing Applicative Landscape
- Invoicing required data & use cases (P2P + intercompany)

6 steps


1. Global Assessment & Impact Analysis
2. French Localization Review
3. Key Business & Design Decisions
4. Data & Integration Assessment
5. Implementation Roadmap & Planning
6. Focus on e-invoicing

Out of scope: Order To Cash (O2C)

Project Management Assistance – Detailed Approach


GT

	1	2	3	4	5	6
	Global assessment & Impact analysis	French localization assessment	Key Business decisions for French localization	Local Data & integration assessment & impact analysis	Implementation Roadmap and Plan - Localization	Focus on e-invoicing
OBJECTIVE	- Identify impacts and challenges in implementing Oracle for France - Review the overall processes that may be impacted by France implementation	- Review and analyze French-specific requirements and their impact on the global system - Ensure compliance with French statutory, tax, regulatory, and banking requirements	Drive key business decisions required to support French localization in oracle ERP	Identify and assess key data migration & integration considerations specific to French requirements	Develop a high-level implementation roadmap and plan for French Localization	Review and analyze French-specific requirements and their impact on the global system
ACTIVITIES	- Confirm scope - Assess overall impacts and challenges: enterprise design, Primary ledgers / COA structure & secondary ledger, multi-GAAP requirements, SLA rules, intercompany invoicing, fixed assets & P2P compliance, project accounting, reporting tools... - Assess the impact of French localization by comparing current global oracle ERP processes with existing French processes - Facilitate workshops - Identify gaps with the core model - Provide a global Impact Assessment report & integration recommendations	- Define and analyze the best target solution that will meet the French requirements - Perform a Fit-Gap analysis to assess which French localization requirements can be supported natively in Oracle SaaS versus those requiring localization extensions: - Tax & statutory reporting - VAT scenarios - E-invoicing/ e-reporting - Banking requirements - Compliance rules - Provide a High-Level Solution design and gap assessment on the French Statutory, Tax, Regulatory & Audit Requirements	- Design solution for France by listing the KDD (Key Design Decisions) to be validated & prepare arbitration committee to select the best solution based on criteria (cost, standard oriented, scalability, etc.) - Topics to be covered: - Ledger Strategy review - COA Alignment - Decision Documentation - Reporting Needs - Formalize key business / Design decisions (KBD/KDD) and ledger strategy / COA alignment recommendations	- Review all topics related to data migration and integration considerations specific to France - Topics to be reviewed: - Data Migration analysis - Integration catalog - Technical Scope Assessment - Banking and Payment Review - Payroll integration - Documentation and Training - Provide data migration recommendations and the required downstream integrations list	- Based on the different elements collected in the Gap Analysis for France, define the high-level implementation roadmap and resource plan for French Localization - Topics to be included: - Implementation Plan - Resource Plan - Risk Management - Future Architecture Recommendations - Stakeholder Alignment	- Evaluate readiness for e-invoicing and e-reporting mandates for France's B2G and B2B transactions: - Invoicing applicative landscape - As-is applicative landscape - To-be applicative landscape - Certified platforms Benchmark - Invoicing required data & use cases - Main P2P use cases - Main Intercompany invoicing use cases - E-invoicing data review (+400 fields for e-invoicing analysis) - Provide a high-level recommendation on France e-invoicing and supporting tool, based on benchmark and REX from France

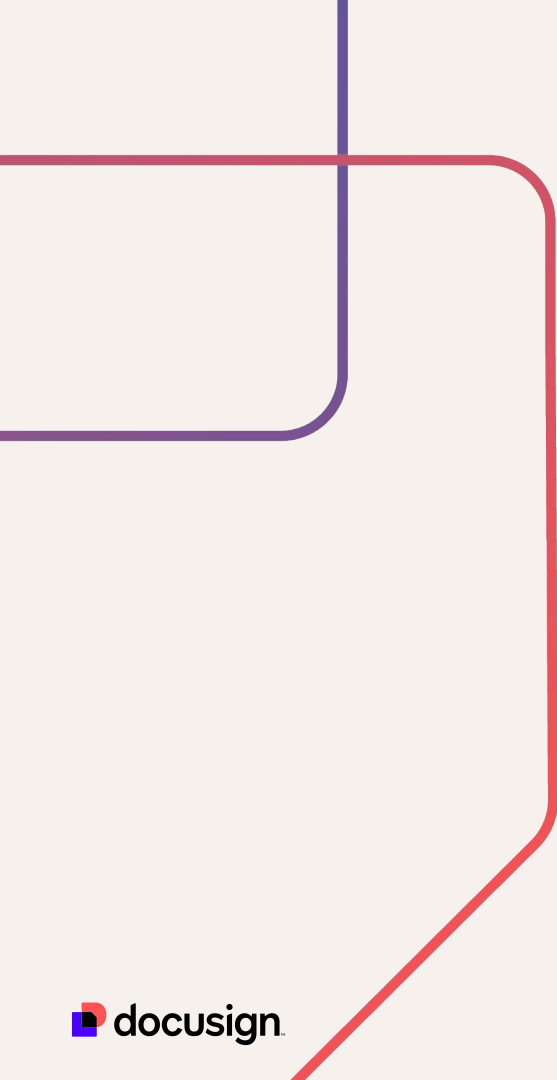


Timeline & Workshop Overview

Grant Thornton: Assessment Timeline

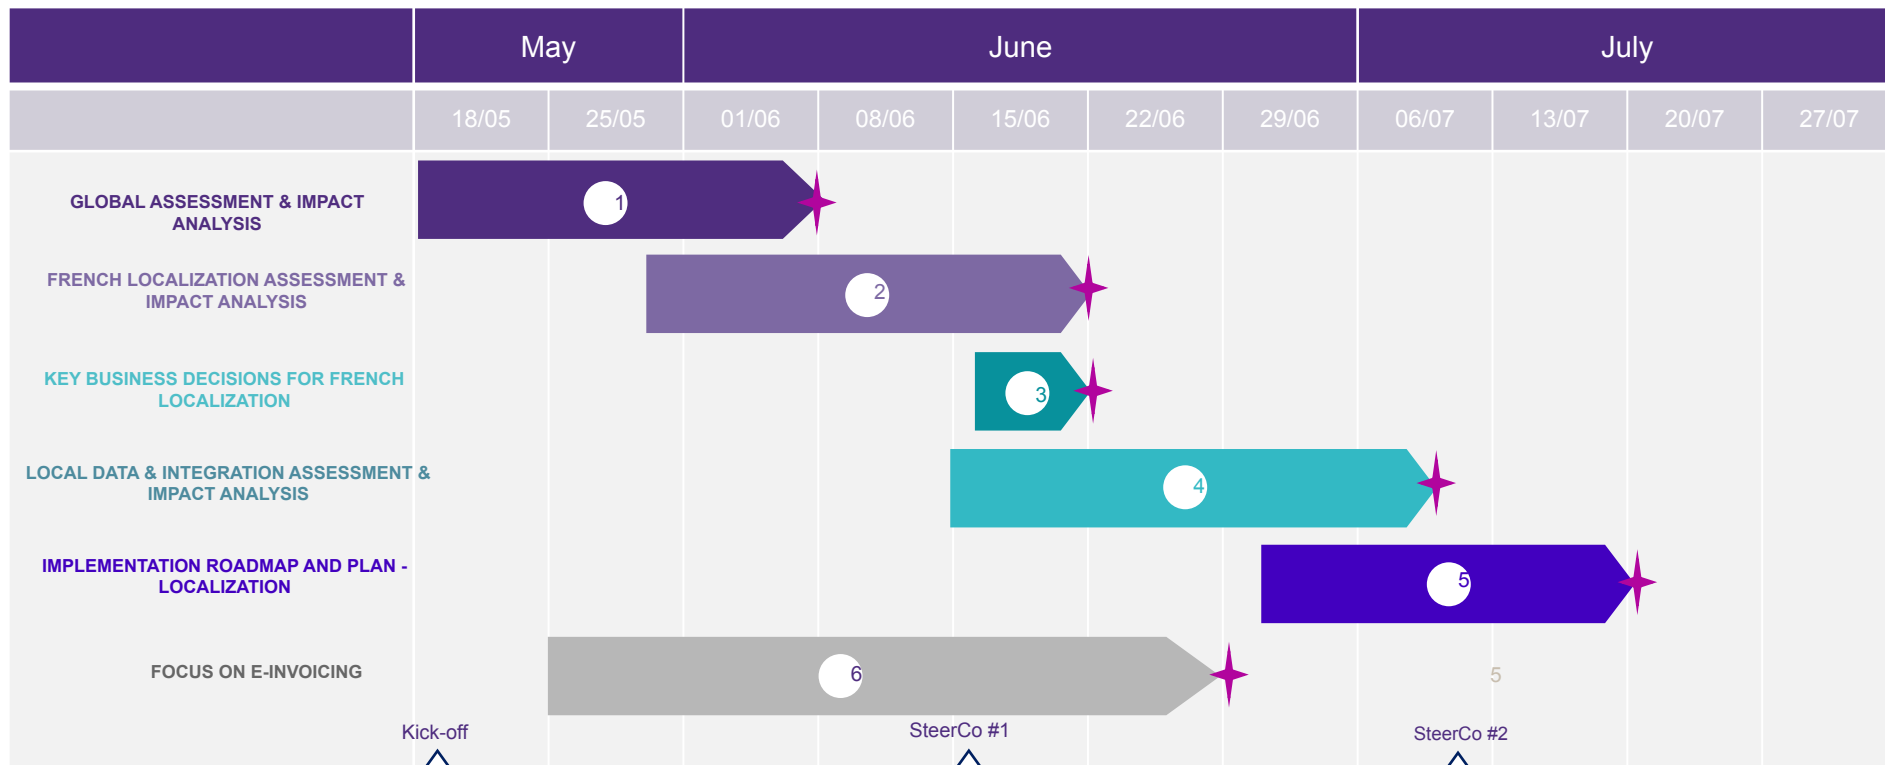


Target Timeline

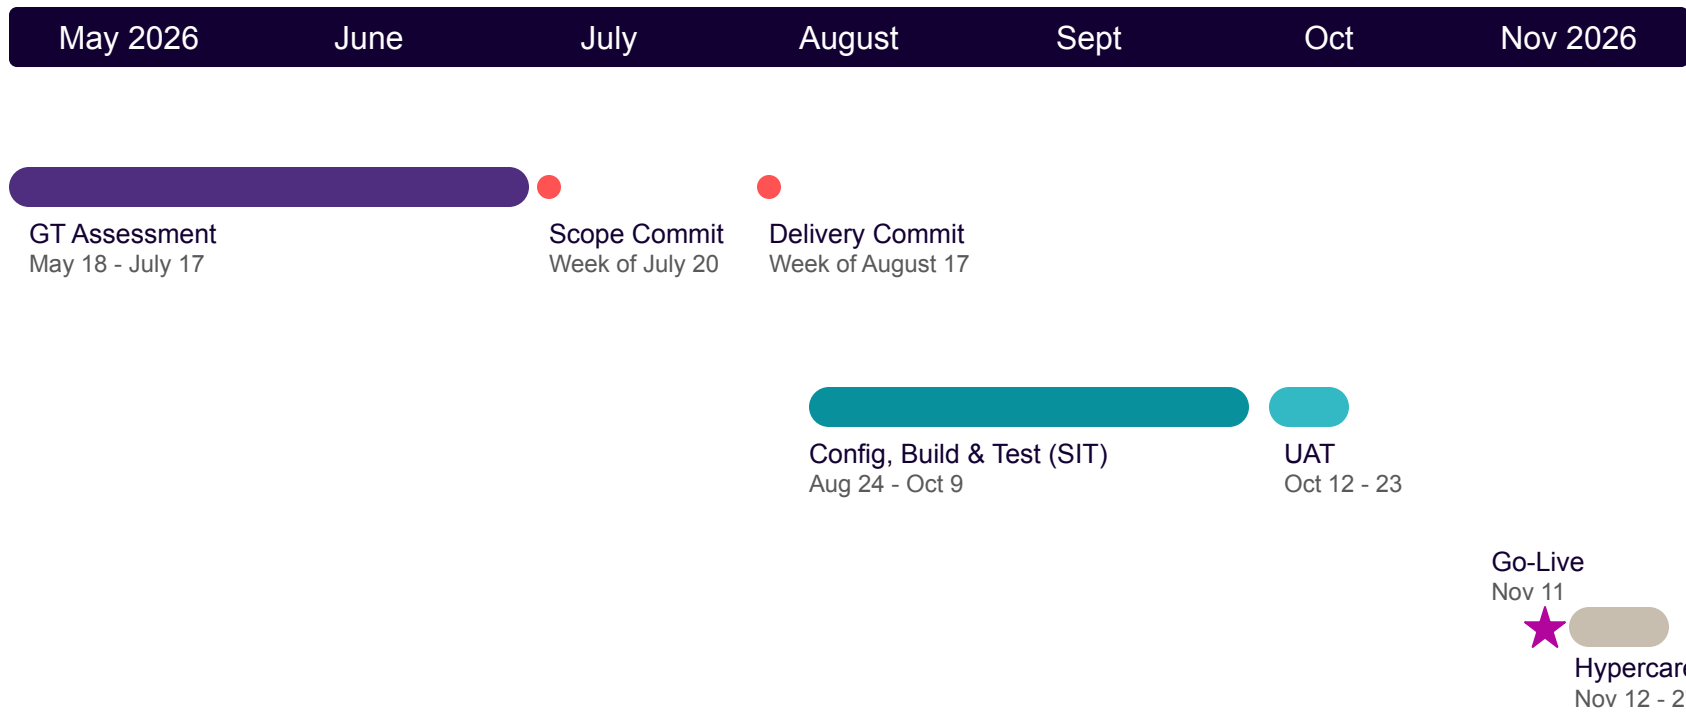

Grant Thornton: Workshops

Workstream	Workshop (2h each)	Topics
1 Global assessment & impact analysis	O2C	Validate it is truly out of scope for French rollout (May still be in scope from a compliance standpoint)
	Enterprise structure	Enterprise, legal entity, BU, accounting key, currency, SLA, CoA, calendar
	R2R	General accounting, fixed assets, VAT, intercompany, closing, Tax & reporting...
	P2P & Cash Management	Procurement, AP, Reporting, Payments, Bank reconciliation
2 French Localization Assessment	Projects	Projects management
	Enterprise structure	Enterprise, legal entity, BU, accounting key, currency, SLA, CoA, calendar
	R2R	General accounting, fixed assets, VAT, intercompany, closing, Tax & reporting...
	P2P & Cash Management	Procurement, AP, Reporting, Payments, Bank reconciliation
3 Key Business Decisions for French Localization	Projects	Projects management
	Enterprise structure	Enterprise, legal entity, BU, accounting key, currency, SLA, CoA, calendar
	R2R	General accounting, fixed assets, VAT, intercompany, closing, Tax & reporting...
	P2P & Cash Management	Procurement, AP, Reporting, Payments, Bank reconciliation
4 Local data & integration assessment & impact analysis	Projects	Projects management
	Data migration #1	Strategy & data analysis
	IT integration #1	Integration analysis
	Data migration #2	Strategy validation & cleansing rules definition
5 Implementation Roadmap & Plan	IT integration #2	Integration validation
	2 Review Workshops	Review the Implementation Roadmap & Plan
	As-is applicative Landscape	As is and ongoing projects
	PA Benchmark	Certified platforms Benchmark
6 Invoicing applicative landscape & Invoicing required data & use cases	To-be applicative Landscape	Target Scenario and invoicing flows
	P2P use cases	Review of applicable P2P use cases
	Intercompany invoicing use cases	Review of applicable Intercompany use cases
	E-invoicing Data #1	Check available Data in Docusign system, map them with the reform required data
	E-invoicing Data #2	
	E-invoicing Data #3	
	E-invoicing Data #4	Determine data that will require enhancements
	E-invoicing Data #5	E-invoicing Data review synthesis

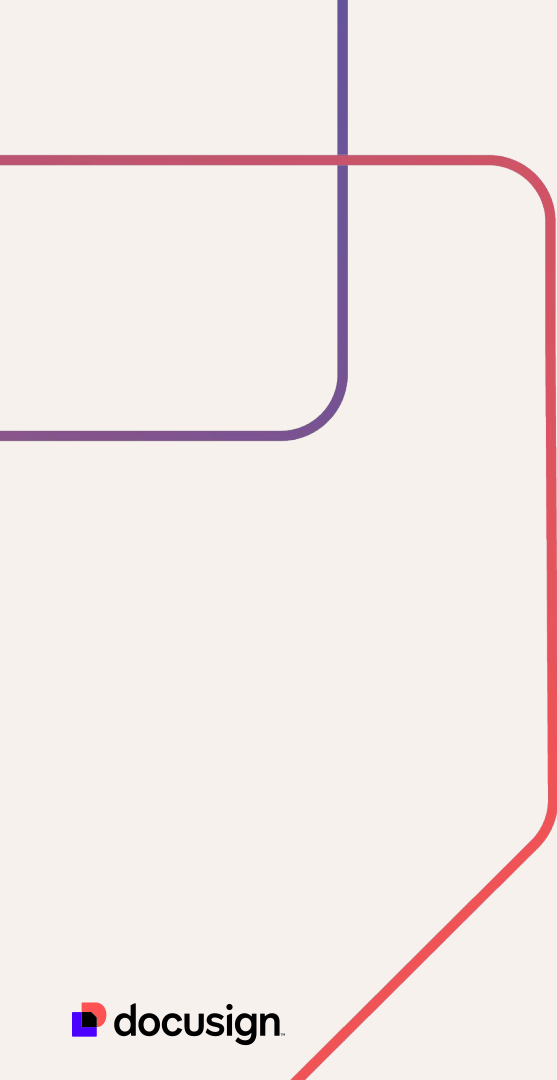

Team & Governance

Grant Thornton Project Team

US GT Team



Bob Allen
US Engagement
Partner



Louise Labrie
Client Relationship
Partner & Quality
Assurance Lead



Al Douglas
US Oracle
Financial Lead

French GT Team



Lydia Lejay
France Lead
Engagement Partner



Romuald Froeliger
France Localization
Lead



Amal Salhi
France Localization
Support



Waldir Cruz
France Localization
Support



Hasnaa Belbaz
France Project
Manager



Amine El Arsi
France E-Invoicing
Lead



Emmanuel Schoemann
France E-invoicing
Support

Docusign Project Team & Leadership Support

Name(s)	Role
Hugo De La Torre	Executive Sponsor
Micheal Kelliher	International Controller
Atul Kakade	Transformation Lead
Eoin Sullivan / Raphaelle Lenoir / Guy Arie	Business Leads
Gina Lin	Change Management Lead
Melissa Scott	Business Program Manager [FBT]
Tina Uh	Business Project Lead [FBT]
Srini Vempati	Functional Lead - Global
Upendra Kondoju / Aswanth Vaidiswaran/ Roger Xu	Engineering Leads

Docusign Project Stakeholders

Name(s)	Team / Group
Jennifer Kearney, Ben Pincon	International Revenue Team
Andrea Wong, Chris Lewis, Jack Hamner	Corporate Accounting
Seydou Konate, Kenza Benabdeljalil	France Accounting Team
Diana Boyd, Matty Cham	AP/Vendor Management
Alen Begovic, Stacy Hernandez	Fixed Assets
Sean Irwin, Wioletta Pietrzak	Intercompany
Steven Crowley, Ernesto Levy, Wendy Gould	Tax
Jennifer Wilhelmsen	Treasury
Jeannine Galliani-Peterson	Procurement
Stacy Hernandez, Ray Pham	Projects

Project Governance & Frequency

Operating Committee (OpCo)

Objectives	Participants	Frequency
- Executive Leadership - Project escalation if needed - Track progress, schedule, and key milestones - Make key trade-offs if necessary (KBDs, KDDs) - Allocate human and material resources - Mobilizing the necessary resources - Validate the service provided and the deliverables	DOCUSIGN - Micheal Kelliher - Atul Kakade - Jay Belur - Eoin Sullivan - Tina Uh - Melissa Scott - Kamlesh Desai	Grant Thornton France - Lydia Lejay - Romuald Froeliger - Hasnaa Belbaz - Waldir Cruz (Tbc) Grant Thornton US - Bob Allen
		- B-Weekly (1 hour) 30 mins GT 30 mins DS

Project Team Meeting

Objectives	Participants	Frequency
- Project status - Project resourcing & scheduling - Raising difficulties - Facilitate the achievement of the assignment - Identify the issues to be escalated to the steering committee for arbitration	DOCUSIGN - Eoin Sullivan - Raphaelle Lenoir - Tina Uh - Melissa Scott - Srini Vempati - Upendra Kondoju	Grant Thornton France - Lydia Lejay - Romuald Froeliger - Waldir Cruz - Hasnaa Belbaz Grant Thornton US - Al Douglas (Tbc)
		Weekly (30min)

Next Steps and Q&A

Next Steps

Confirm Workshop Participants & Finalize Schedule

- Targeting May 26 - June 25

Responsible POC: Melissa Scott in coordination with EMEA Finance and GT

Complete By
May 22

Schedule Recurring Meetings

- OpCo Meeting
- Project Team Meeting

Responsible POC: Melissa Scott

Complete By
June 2




Project Management Assistance – Deliverables

1 - GLOBAL ASSESSMENT & IMPACT ANALYSIS	2 - French localization assessment	3 - Key Business decisions for French localization
▪ Support Kick Off ▪ Support for validated workshops ▪ Global Impact Assessment report, detailing potential impacts and challenges: List of global processes impacted due to French localization requirements ▪ Recommendations on integration and adaptation needs	▪ High-Level Solution design and gap assessment on the French Statutory, Tax, Regulatory & Audit Requirements ▪ List of RICEW Objects for all GAP requirements ▪ List of the documents & content required in the local language ▪ Intercompany invoicing process Impact and recommendations ▪ Recommendations on France e-invoicing and supporting tool ▪ High-level solution for implementing the e-invoicing for France entity and recommendations on the foundational e-invoicing platform	▪ Key Business Decisions and Key Design Decisions: details, pros and cons and recommended decisions ▪ Recommendations for ledger strategy and COA alignment
4 - Local DATA & integration assessment & impact analysis	5 - Implementation Roadmap and Plan – Localization	6 - Focus on e-invoicing
▪ Recommendations on the key data migration (data and migration strategy for meeting local French requirements) ▪ List of required upstream & downstream integrations, including a catalog of in-scope downstream integrations (e.g. banks, tax authorities, e-invoicing), including high-level architecture considerations.	▪ High-level implementation plan for localization ▪ Resource Plan, including a high-level detailed implementation cost estimate for the France localization ▪ Issues, Risks, and Dependencies ▪ Future state architecture recommendations	▪ Recommendations on France e-invoicing and supporting tool ▪ High-level solution for implementing the e-invoicing for France entity and recommendations on the foundational e-invoicing platform

Project Roles and Definitions

Role Name	Description
FBT Project Lead	Accountable for overall execution, risk management/escalation, and proactive communication back to FBT leadership, portfolio owner, and supporting team members. Drives key milestones such as ○ Business Solution Design (Scope Commit, KBDs/KDDs) ○ Business requirements (BRDs) ○ UAT Timeline and Use Cases ○ Hypercare Planning
Product Manager	Solution architect who partners with the FBT project lead and other business stakeholders on requirements finalization and close-out of KDDs. Serves as the liaison to the engineering team to review design details, demo preparation and configuration.
Technical Project Manager/SME	Owns the day to day technical project delivery and plan and providing status to the FBT Lead and Business Program Manager. Assist in preparing functional spec, configurations and liaises with developers on reports development/unit testing and scheduling sprint demos.
Application Functional Lead	Responsible for functional design, testing and troubleshooting.
Application Engineering Lead	Supports technical build, execution, configuration and delivery of solution.
FBT Program Manager	Responsible for overarching program management of all CAO initiatives. Manages program governance and facilitates key meetings such as SteerCo, OpCo, Scope/Delivery Commits, and Go/No-Go calls. Monitors risks and assists with project escalations as needed.
Change Lead	Owns overarching change strategy and management of the project change plan.
Contractors	Any external contractors supporting project delivery and execution (roles may differ depending on SOW).

Grant Thornton Assessment Approach

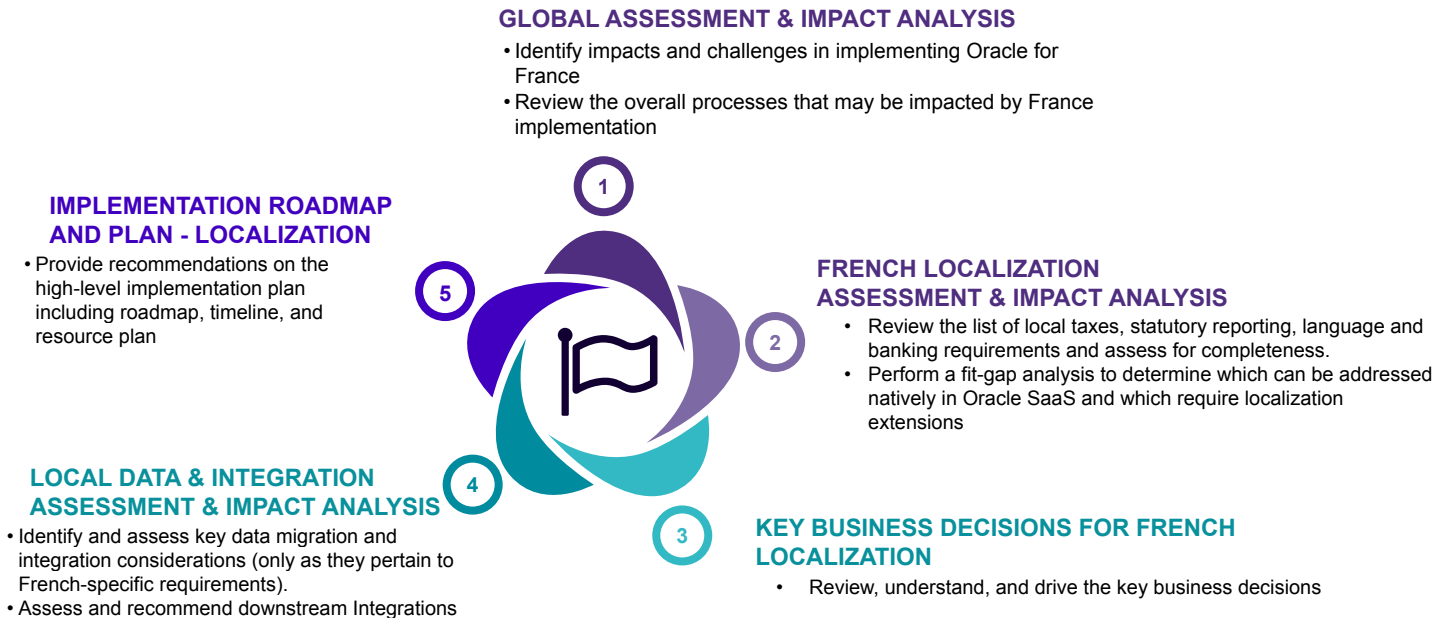

Project Management Assistance – Detailed approach

3

KEY BUSINESS DECISIONS FOR FRENCH LOCALIZATION

OBJECTIVES



- Drive key business decisions required to support French localization in Oracle ERP

Design solution for France: list the Key Design Decisions (KDD) to be validated and prepare arbitration committees to select the best solution based on criteria (cost, standard oriented, scalability, etc.)

The KDD must at least cover the following topics :

- **Ledger Strategy Review:** Examine the entity structure, ledger design, legal reporting, and multi-GAAP considerations (US GAAP vs French GAAP)
- **COA Alignment:** Align the global Chart of Accounts (COA) with the French Chart of Accounts (Plan Comptable Général)
- **Decision Documentation:** Document all key business decisions made during the localization process
- **Reporting Needs:** Identify additional reporting or analytics requirements specific to French localization
- **Drive key business decisions** required to support French localization in Oracle ERP

DELIVERABLES



- Key Business Decisions and Key Design Decisions: details, pros and cons and recommended decisions
- Recommendations for ledger strategy and COA alignment

ACTIVITIES



Prerequisites

- Access to current COA and ledger structures
- Participation of management for strategic decisions

Cost drivers

- 4 Workshops – 2 hours each
- 1 KDD validation meeting

Project Management Assistance – Detailed approach

4

LOCAL DATA & INTEGRATION ASSESSMENT & IMPACT ANALYSIS

OBJECTIVES



- Identify key data migration and integration considerations specific to French requirements

Organize workshops to review all topics related to data migration and integration considerations specific to France. The topics to be reviewed are at least the following :

- **Data Migration Analysis:** Evaluate the impact of data migration concerning French GAAP and localization requirements
- **Integration Catalog:** Build a catalog of required downstream integrations, including banking APIs and e-invoicing
- **Technical Scope Assessment:** Analyze the technical scope, extension needs, and reporting configurations
- **Banking and Payment Review:** Review bank connectivity and formats, ensuring compliance with payment approvals and security mandates
- **Payroll Integration:** Outline payroll integration requirements and unique posting, allocation, or accrual practices
- **Documentation and Training:** Ensure all project documentation and training materials are provided bilingually

DELIVERABLES



ACTIVITIES



- Recommendations on the key data migration (data and migration strategy for meeting local French requirements)
- List of required upstream & downstream integrations, including a catalog of in-scope downstream integrations (e.g. banks, tax authorities, e-invoicing), including high-level architecture considerations.

Prerequisites

- Access to existing data migration processes documentation
- Availability of technical teams for integration assessments

Cost drivers

- 4 Workshops – 2 hours each
- 1 validation meeting

Project Management Assistance – Detailed approach

5

IMPLEMENTATION ROADMAP AND PLAN - LOCALIZATION

OBJECTIVES



- Develop an implementation roadmap and plan for French localization

Based on the different elements collected in the Gap Analysis for France, define the implementation roadmap and resource plan. The below topics need to be included in this step :

- **Implementation Plan:** Build a high-level implementation plan, including roadmap, timeline, key milestones, project phases...
- **Resource Plan:** Provide a plan, including the resources required to support Localization
- **Risk Management:** Identify potential risks, issues, dependencies and develop mitigation strategies
- **Future Architecture Recommendations:** Suggest future state architecture for integration and associated systems
- **Stakeholder Alignment:** Ensure all stakeholders are aligned regarding project scope and timelines

Organize a validation session to present and to validate the implementation roadmap for French localization.

DELIVERABLES



- High-level implementation plan for localization
- Resource Plan, including a high-level detailed implementation cost estimate for the France localization
- Issues, Risks, and Dependencies
- Future state architecture recommendations

ACTIVITIES



Prerequisites

- Agreement on project scope and timelines from all stakeholders
- Availability of resources and budget for implementation

Cost drivers

- 2 review and validation meetings

Project Management Assistance – Detailed approach

Focus on e-invoicing

OBJECTIVES

- Evaluate readiness for e-invoicing and e-reporting mandates for France's B2G and B2B transactions
 - **Invoicing applicative landscape:**
 - As Is applicative landscape
 - To Be applicative landscape
 - Certified platforms Benchmark
 - **Invoicing required data & use cases:**
 - Main P2P use cases identification
 - Main O2C use cases identification
 - e-invoicing data review (+400 fields for e-Invoicing analysis)
- **Provide a high-level recommendation on France e-invoicing and supporting tool**, based on benchmark and REX from France

DELIVERABLES

- **Review and analyze French-specific requirements and their impact on the global system**

ACTIVITIES

Prerequisites

- Data and documentations should be provided ahead the workshops.
- SME should be available

Methodology

- 3 IS Workshops
- 2 Use cases Workshops
- 4 data review workshops
- 1 validation meeting

- **Recommendations on France e-invoicing and supporting tool**
- **High-level solution for implementing the e-invoicing for France entity and recommendations on the foundational e-invoicing platform**

Project Team with Roles

Project	Business Teams (Roadmap, Scope, Budget, Requirements)		Technical Teams (Design to Delivery)				Support Teams (Change Mgmt, Contractors, QA, Release Mgmt, etc).	
	FBT Project Lead	Business Leads	Product Manager	Tech Project Manager/ SME	Application Functional Lead	Technical Developers	Change Lead	Contractors
France Entity Migration	Tina Uh	Micheal Kelliher - Global Accounting Vichheka Heang - Global Accounting (I) Eoin Sullivan, Raphaelle Lenoir - Accounting Lead (s) Atul Kakade - CAO Transformation Lead	Srini Vempati	TBD	Aswanth Vaidiswaran Roger Xu			GrantThorton

Executive Sponsor	Hugo De La Torre
CAO Initiatives - DRI (Directly Responsible Individual)	Micheal Kelliher
FBT Program Manager	Melissa Scott
FBT Leadership	Alex Kanias

Executive Summary



Objectives

Migrate French legal entity accounting processes and data from Sage to Global Oracle Fusion

AND

Migrate DS France active customer contracts to DS EMEA



Opportunity

By migrating French legal entity to Global Oracle Fusion, we will be able to:

- Retire local ERP (Sage)
- Globalize AP to improve controls and reduce SOD issues
- Globalize Record to Report (R2R) process with the same chart of accounts
- Implement standard global SOX controls
- Provide real time access to DS France accounts to Corporate teams
- Automate accounting processes in line with the global process (including billing and revenue)
- Reduce manual reporting
